Appendix XVIII
State Construction Tentative Timeline
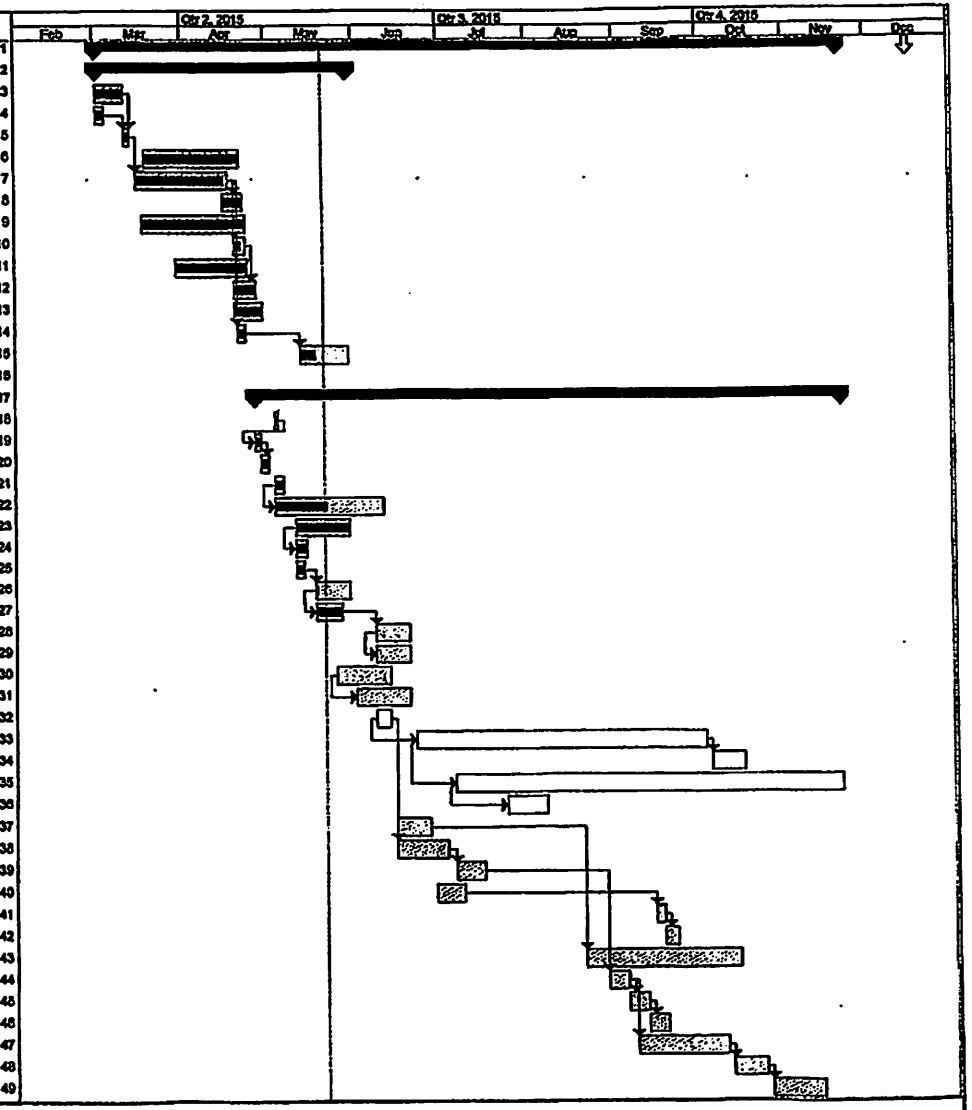
ID	Task Name	Duration	Start	Finish	Physical % Complete	Percentage Complete
1	Marina At Caesar Creek	190 days	Mon 3/2/15	Fri 11/20/15	0%	1
2	Phase 1 A	55 days	Mon 3/2/15	Fri 6/29/15	0%	2
3	Clearing and Mowing	6 days	Mon 3/2/15	Wed 3/11/15	100%	3
4	Silt Fence and Tree Fence	3 days	Mon 3/2/15	Wed 3/4/15	100%	4
5	Strip Wetlands and Stock	2 days	Thu 3/12/15	Fri 3/13/15	100%	5
6	Delivery Of Rip Rap and 1's For Slope	24 days	Thu 3/19/15	Tue 4/21/15	100%	6
7	Excavation of Lake (1A)	25 days	Mon 3/16/15	Fri 4/17/15	100%	7
8	Dock/Attenuator Anchors	5 days	Thu 4/15/15	Wed 4/22/15	80%	8
9	Bedding Stone/Rip Rap	27 days	Wed 3/18/15	Thu 4/23/15	100%	9
10	Trees, Logs, Cobble	4 days	Mon 4/20/15	Thu 4/23/15	100%	10
11	Stacking Block Stone	20 days	Mon 3/30/15	Fri 4/24/15	100%	11
12	Fish Spawning Bed	4 days	Mon 4/20/15	Mon 4/27/15	100%	12
13	Emergent Planting Area, Grade/Topsoil	6 days	Mon 4/20/15	Wed 4/29/15	100%	13
14	42"/48" Storm Pipe	3 days	Tue 4/21/15	Thu 4/23/15	100%	14
15	Landscaping In Emergent Planting	13 days	Wed 5/13/15	Fri 5/29/15	25%	15
16						16
17	Phase 1 B	150 days	Mon 4/27/15	Fri 11/20/15	0%	17
18	Silt Fence	1 day	Mon 5/4/15	Mon 5/4/15	100%	18
19	Strip Topsoil	2 days	Mon 4/27/15	Tue 4/28/15	100%	19
20	Cut To Fill	3 days	Wed 4/29/15	Fri 5/1/15	100%	20
21	2" Sanitary To Dock	3 days	Mon 5/4/15	Wed 5/6/15	95%	21
22	76" Oliptical Pipe/ End Walls	28 days	Mon 5/4/15	Wed 6/10/15	50%	22
23	Weir Wall	15 days	Mon 5/11/15	Fri 5/29/15	95%	23
24	Waterline 6", 4", Hydrant	4 days	Mon 5/11/15	Thu 5/14/15	95%	24
25	Respread Topsoil, First Half Of Job	3 days	Mon 5/11/15	Wed 5/13/15	100%	25
26	Landscape/Seeding On First Half Of Job	10 days	Mon 5/18/15	Fri 5/29/15	5%	26
27	Storm Pipe, Strucuros, End Walls	7 days	Mon 5/18/15	Tue 5/26/15	100%	27
28	Remaining Utilities To Dock	10 days	Mon 6/8/15	Fri 6/19/15	0%	28
29	Concrete For Signage/Bridge	10 days	Mon 6/8/15	Fri 6/19/15	0%	29
30	Stream Channels Phase B	15 days	Mon 5/25/15	Fri 6/12/15	0%	30
31	Timber Bridge	15 days	Mon 6/1/15	Fri 6/19/15	0%	31
32	Gangway Abutments	5 days	Mon 6/8/15	Fri 6/12/15	0%	32
33	Install Attenuators/Docks	75 days	Mon 6/22/15	Fri 10/2/15	0%	33
34	Fuel Attendant Bldg/Fueling System	10 days	Mon 10/5/15	Fri 10/16/15	0%	34
35	Marina Building	100 days	Mon 7/6/15	Fri 11/20/15	0%	35
36	Utilities To Marina Building	10 days	Fri 7/24/15	Thu 8/6/15	0%	36
37	Utilities/Lights On Site	10 days	Mon 6/15/15	Fri 6/26/15	0%	37
38	Concrete Wall/Stone, Drop Off	14 days	Mon 6/15/15	Thu 7/2/15	0%	38
39	Curbs And Sidewalks	6 days	Mon 7/6/15	Wed 7/15/15	0%	39
40	304 Stone In Parking Lot	6 days	Mon 6/29/15	Wed 7/8/15	0%	40
41	Asphalt In Parking Lot	3 days	Mon 9/14/15	Wed 9/16/15	0%	41
42	Parking Lot Striping/Blocks	3 days	Thu 9/17/15	Mon 9/21/15	0%	42
43	Utilities/ Signage For Docks	40 days	Thu 8/20/15	Wed 10/14/15	0%	43
44	Fine Grade	5 days	Fri 8/28/15	Thu 9/3/15	0%	44
45	Respread Topsoil/Fine Grade Site	5 days	Fri 9/4/15	Thu 9/10/15	0%	45
46	Signage For Entire Site	5 days	Fri 9/11/15	Thu 9/17/15	0%	46
47	Landscaping/Seeding Last Half	25 days	Mon 9/7/15	Fri 10/9/15	0%	47
48	Punchout and Cleanup	10 days	Mon 10/12/15	Fri 10/23/15	0%	48
49	Closeout Job	14 days	Mon 10/26/15	Thu 11/12/15	0%	49
